



SUPPLEMENTAL INSTRUCTION

CONTRACTOR:
Tal-co Building Innovations
Address:
Suite 2, 1341 Coker Street
Greely, Ontario, K4P 1A1

PROJ.: **Boys and Girls Club Prince of Wales**
PROJ. No.: **1716**
DATE: **May 31, 2018**
S.I. No. **S.I. - 028**

Supplemental Instructions are issued to the Construction Manager to record a clarification or revision to the previously issued Contract Documentation as reflected by the attached Information Bulletin prepared by the identified Consultant.

The Construction Manager shall review the Supplemental Instruction and the attached Information Bulletin and issue to the effected Trade Contractors identifying the following course of action by the trade contractor:

- Proceed with Instruction. Issued for general information, no change to Contract price or schedule. (Site Instruction)
- Proceed with Instruction and provide a quotation within 10 days, identifying change to Contract price and schedule (Change Directive)
- Do not proceed. Provide quotation identifying change to Contract price and schedule within 10 days. (CCO)

Partners

Barry J. Hobin
OAA, FRAIC, Hon. Fellow AIA

William A. Davis
OAA, MRAIC, Associate AIA

Gordon Lorimer
OAA, FRAIC, Associate AIA

Wendy Brawley
OAA, MRAIC, Associate AIA

Douglas Brooks
Senior Arch. Tech.

Associates

Bryan Bonell
OAA, MRAIC, Associate AIA

Marc Thivierge
OAA, MRAIC

William Ritcey
MRAIC

Reinhard Vogel
Senior Arch. Tech.

1.1 TITLE
Revision of Lighting Control System

1.2 DESCRIPTION OF THE WORK
.1 Delete photocell detectors
.2 Delete exterior lighting time clock

1.3 ATTACHMENTS
BGCO-ECCN-04

1.4 REASON
Above noted components are not needed for the system as Vive Hub lighting control will handle these functions.

Hobin Architecture Incorporated


63 Pamilla Street
Ottawa, Ontario
Canada K1S 3K7

t 613-238-7200
f 613-235-2005

hobinarc.com

Distribution:

- | | | | | |
|--|--|--|----------------------------------|--------------------------------------|
| <input checked="" type="checkbox"/> Owner | <input type="checkbox"/> City Authority | <input checked="" type="checkbox"/> Electrical | <input type="checkbox"/> Struct. | <input type="checkbox"/> Landscaping |
| <input checked="" type="checkbox"/> Contractor | <input checked="" type="checkbox"/> File | <input type="checkbox"/> Mech. | <input type="checkbox"/> Civil | <input type="checkbox"/> Other |

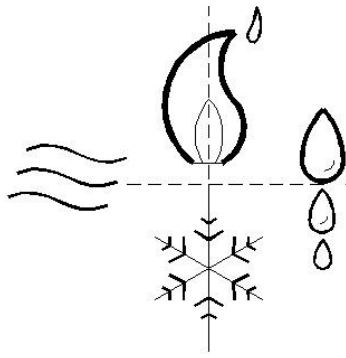

BEKOLAY & Associates. Ltd.

Consulting Engineers

Electrical Contemplated Change Notice (ECCN)

Consultant:	Barry J. Hobin & Associates Architects 63 Pamilla St. Ottawa On. K1S 3K7	Project:	Boys & Girls Club P.O.W. 1463 Prince of Wales
Contractor:	Tal-Co Andrew King	BAL No.:	2017-17
Attn:	Doug van den Ham Sandy Davis	MCCN#	ECCN-04
		Date:	2018-05-30

Provide a firm price for the modifications to the project described below, identifying the material and labour cost breakdowns for such changes, including credits and extras as applicable. No work should be undertaken until a Change Order or written authorization has been signed and issued. The work shall conform to the contract documents where applicable unless otherwise stated.

See issued for construction drawings & lighting control submittal

1. See Drawings E-5, E-8
 - a. Delete photocell detectors, Lutron Vive Hub will provide time clock control
 - b. Delete Exterior lighting time clock, Lutron Vive Hub will provide time clock control

Link to lighting control submittal:

https://fluxlighting-my.sharepoint.com/personal/emerson_fluxlighting_ca/_layouts/15/onedrive.aspx?id=%2Fpersonal%2Femerson_fluxlighting_ca%2FDocuments%2F17797%20-%20Boys%20%26%20Girls%20Club%20-%20Submittal%20%282018%2E05%2E22%29%20R%2E4%2Epdf&parent=%2Fpersonal%2Femerson_fluxlighting_ca%2FDocuments&slrid=e7986b9e-60db-5000-d7a1-1ea172cdc283
