

## GENERAL NOTE(S):

- 1- ALL EXISTING PIPING, THIS INCLUDES DCW, DHW, VENTS, STORM AND SANITARY DRAINAGE AT CEILING LEVEL TO REMAIN, SOME SECTIONS WILL REQUIRE SOME REPLACEMENT, SEE NEW LAYOUT.
- 2- SOME REMOVAL WILL BE REQUIRED AS INDICATED ON DRAWING. SOME SECTIONS OF PIPING ARE DAMAGED OR HAVE BEEN PULLED DOWN. THESE SECTIONS ARE TO BE REMOVED. RECYCLE EXISTING VALVES THAT HAVE ALREADY BEEN INSTALLED IF POSSIBLE. (BALL VALVES MOSTLY)
- 3- ALL EXISTING PIPE SUPPORTS WILL HAVE TO BE VERIFIED AND REPLACED AS NECESSARY, SOME MAY HAVE BEEN RIPPED OUT. PROVIDE FOR 20% REPLACEMENT ON PIPING THAT REMAINS. ALL OTHER PIPE SUPPORTS NOT USED OR DAMAGED ARE TO BE REMOVED COMPLETELY.
- 4- FOR INFORMATION ONLY. PIPING MATERIAL FOR CONDENSATE DRAINAGE SHOWN ON DRAWING IS AS FOLLOWS. MAIN PIPING IS IN XFR PLASTIC PIPING AND SIDE BRANCHES ARE COPPER LINES.
- 5- FOR INFORMATION ONLY. PIPING MATERIAL FOR STORM AND SANITARY DRAINAGE SHOWN ON DRAWING IS AS FOLLOWS. ALL PIPING IS IN XFR PLASTIC PIPE. THIS INCLUDES SIDE BRANCHES UP TO CONNECTION. NO CONNECTIONS OR FLANGE FOR CONNECTION TO A FIXTURE HAVE BEEN INSTALLED. IF ANY REMOVE AND REPLACE.

## IDENTIFICATION(S):

- 1 SEE MODIFICATIONS TO SANITARY UNDER THE SLAB ON DRAWING M-200. 4" MAIN TO BE REPLACED WITH 6"Ø MAIN FROM BASEMENT TO CONNECTION TO MAIN 6"Ø IN FRONT ROOM. SLAB TO BE OPENED FOR MODIFICATIONS AND REPLACED BY GENERAL CONTRACTOR WHEN ALL WORK IS COMPLETED.
- 2 EXISTING GAS LINE PART OF TEMPORARY SERVICE TO REMAIN IN PLACE UNTIL SERVICE IS RELOCATED OR BUILDING IS MODIFIED.
- (3) EXISTING GAS LINE PART OF TEMPORARY HEATING LOOP. TO BE REMOVED WHEN WINTER HEATING IS NO LONGER REQUIRED, COORDINATE WITH GENERAL CONTRACTOR.
- 4 > SECTIONS OF DCW, DHW AND DHWR TO BE CUT AND PREPARED TO BE REUSED FROM THIS POINT ON. SECTIONS SHOWN IN HIDDEN LINES ARE TO BE REMOVED. SEE NEW LAYOUT FOR NEW PIPING.
- 5 PIPE SUPPORT ON EXISTING PIPING WAS RIPPED OUT AND THE PIPING IS HANGING LOOSE. REPLACE PIPE SUPPORT.
- 6 PRESENTLY DCW, DHW AND DHWR ARE CONNECTED TOGETHER FOR PRESSURE TESTING. INTERCONNECTION TO BE REMOVED ONCE PRESSURE TEST IS DONE.
- 7 PRESENTLY VENT, SANITARY OUTLET AND CONDUIT FOR THE ELEVATOR SUMP PIT FLOATS SYSTEM ARE COMING OUT OF THE SLAB AT THIS LOCATION -AND ARE CAPPED AT 3' FROM THE GROUND. SEE CONTINUATION ON NEW
- ( 8 ) EXITING STORM DRAIN RISER CURRENTLY IN CAST IRON PIPE TO BE REMOVED AND REPLACED BY NEW XRF PLASTIC PIPING. FROM CEILING ON GROUND FLOOR TO THE UNDER SIDE OF THE ROOF
- 9 EXISTING GAS METER, HEADER AND VALVES TO BE REMOVED BY ENBRIDGE AND NEW GAS METER TO BE RELOCATED BEHIND GYMNASIUM. SEE NEW LAYOUT DRAWING FOR NEW LOCATION.
- $\langle$  10  $\rangle$  EXISTING FLOOR SLAB WILL TO BE OPENED FOR MODIFICATIONS BY GENERAL CONTRACTOR. SEE NEW LAYOUT FOR MODIFICATIONS TO EXISTING \_ PLUMBING STUBS AND REVISED LAYOUT OF ROOM.


THIS DRAWING IS ISSUED FOR DEMOLITION PURPOSES, IT REPRESENTS AN INVENTORY OF THE MAIN EXISTING INSTALLATIONS, GENERALLY VERIFIED IN CONNECTION WITH

THE MODIFICATIONS SHOWN ON THIS

DRAWING'S "MODIFIED" VERSION, AND OF


WHICH THE GENUINE CONDITIONS MUST BE

OBSERVED ON THE SITE BY THE CONTRACTOR.

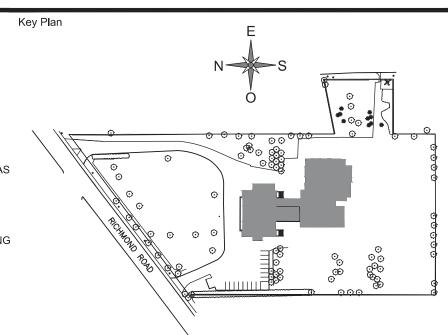

<u> </u>				
N°	Date	Description		
0	2018-06-01	FOR TENDER		

	0	2018-06-01	FOR TENDER
)			
)			
RE			







Structure



MAISON DE DE LA FRANCOPHONIE D'OTTAWA

2720 RICHMOND ROAD, OTTAWA

MECHANICAL **PLUMBING GROUND FLOOR DEMOLITION** 

Project n°: 7342-001-000 2018-06-01 Verified by : F. DIONNE 1/8" = 1'-0"

Drawing n⁰

MD-201
